Name Of work : - Improvements to Roads and Drains at Amruthahalli Village, Hoodi Layout, Tala cauvery Layout and Surrounding Areas in Ward No 07 Byatrayanapura, Kodigehalli Sub Division

BOQ Item No	Description Chainage		Side	Nos	L	B1	B2	Avg width	Depth	Quantity	Remarks
	30.00	45.00		1.00	15.00	7.85	7.55	7.70		115.50	
	45.00	60.00		1.00	15.00	7.55	6.94	7.25		108.68	
	60.00	75.00		1.00	15.00	6.94	8.75	7.85		117.68	
	75.00	90.00		1.00	15.00	8.75	7.14	7.95		119.18	
	90.00	105.00		1.00	15.00	7.14	7.55	7.35		110.18	
	105.00	120.00		1.00	15.00	7.55	7.44	7.50		112.43	
	120.00	135.00		1.00	15.00	7.44	7.55	7.50		112.43	
	135.00	150.00		1.00	15.00	7.55	9.65	8.60		129.00	
	150.00	165.00		1.00	15.00	9.65	7.54	8.60		128.93	
	165.00	180.00		1.00	15.00	7.54	7.75	7.65		114.68	
	180.00	195.00		1.00	15.00	7.75	8.54	8.15		122.18	
	195.00	210.00		1.00	15.00	8.54	7.85	8.20		122.93	
	210.00	230.00		1.00	20.00	7.85	8.84	8.35		166.90	
	Chitrakut Apt Road										
	0.00	15.00		1.00	15.00	5.70	5.29	5.50		82.43	
	15.00	30.00		1.00	15.00	5.29	6.20	5.75		86.18	
	30.00	45.00		1.00	15.00	6.20	4.50	5.35		80.25	
	45.00	47.00		1.00	2.00	4.50	6.00	5.25		10.50	
	Govindappa badavane 1st Cross Road										
	0.00	15.00		1.00	15.00	6.50	5.10	5.80		87.00	
	15.00	30.00		1.00	15.00	5.10	6.20	5.65		84.75	
	30.00	45.00		1.00	15.00	6.20	6.30	6.25		93.75	
	45.00	57.00		1.00	12.00	6.30	6.30	6.30		75.60	
	Hoodi badavane 2nd main Road										
	0.00	15.00		1.00	15.00	4.10	4.10	4.10		61.50	
	15.00	30.00		1.00	15.00	4.10	3.70	3.90		58.50	
	30.00	45.00		1.00	15.00	3.70	3.50	3.60		54.00	
	45.00	60.00		1.00	15.00	3.50	3.70	3.60		54.00	
	60.00	75.00		1.00	15.00	3.70	4.40	4.05		60.75	
	75.00	90.00		1.00	15.00	4.40	4.30	4.35		65.25	
	90.00	99.00		1.00	9.00	4.30	4.50	4.40		39.60	
						Total Quantity				**12676.91**	**Cum**

Consultant

For M/s. RAM & COMPANY
Partner

Assistant Engineer
AE(W) 19/2/18

Assistant Executive Engineer
19/2
Assistant Executive Engineer,
Kodigehalli Sub Division,
Yelahanka Zone, B.B.M.P.,
Bangalore.

67

Name Of work : - Improvements to Roads and Drains at Amruthahalli Village, Hoodi Layout, Tala cauvery Layout and Surrounding Areas in Ward No 07 Byatrayanapura, Kodigehalli Sub Division

BOQ Item No	Description / Chainage		Side	Nos	L	B1	B2	Avg width	Depth	Quantity	Remarks
28	KSRRB M500-16. Providing and laying dense bituminous macadam 50-75mm compacted thickness with 4.5% VG-30 Bitumen using 40/60 TPH capacity H.M.P, using crushed aggregates of grading II, premixed with VG 30 grade bituminous binder and transporting the hot mix to work site, laying with mechanical paver to the required grade level and alignment rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction as per MORTH table 500-10, complete in all respects complete as per specification MORTH specification No. 507 (P.No.162 I.No. 21.17.6 of PW,P&IWTD S.R 2016-17)										
	Hoodi Layout Main Road										
	0.00	15.00		1.00	15.00	3.00	3.10	3.05	0.05	2.29	
	15.00	30.00		1.00	15.00	3.10	3.10	3.10	0.05	2.33	
	30.00	45.00		1.00	15.00	3.10	3.19	3.15	0.05	2.36	
	45.00	60.00		1.00	15.00	3.19	3.00	3.10	0.05	2.32	
	60.00	75.00		1.00	15.00	3.00	3.10	3.05	0.05	2.29	
	75.00	90.00		1.00	15.00	3.10	3.20	3.15	0.05	2.36	
	90.00	105.00		1.00	15.00	3.20	3.09	3.15	0.05	2.36	
	105.00	120.00		1.00	15.00	3.09	3.00	3.05	0.05	2.28	
	120.00	141.00		1.00	21.00	3.00	3.09	3.05	0.05	3.20	
	141.00	156.00		1.00	15.00	3.09	3.00	3.05	0.05	2.28	
	156.00	171.00		1.00	15.00	3.00	3.00	3.00	0.05	2.25	
	171.00	185.00		1.00	14.00	3.00	3.10	3.05	0.05	2.14	
	185.00	200.00		1.00	15.00	3.10	3.10	3.10	0.05	2.33	
	200.00	215.00		1.00	15.00	3.10	3.20	3.15	0.05	2.36	
	215.00	230.00		1.00	15.00	3.20	3.00	3.10	0.05	2.33	
	230.00	245.00		1.00	15.00	3.00	3.00	3.00	0.05	2.25	
	245.00	260.00		1.00	15.00	3.00	3.09	3.05	0.05	2.28	
	260.00	275.00		1.00	15.00	3.09	3.00	3.05	0.05	2.28	
	275.00	290.00		1.00	15.00	3.00	3.10	3.05	0.05	2.29	
	290.00	305.00		1.00	15.00	3.10	3.00	3.05	0.05	2.29	
	305.00	320.00		1.00	15.00	3.00	3.19	3.10	0.05	2.32	
	320.00	334.00		1.00	14.00	3.19	3.20	3.20	0.05	2.24	
	Talakaveri Layout-SBI Bank Road										
	LHS										
	0.00	15.00		1.00	8.00	0.50	0.60	0.55	0.05	0.22	
	15.00	30.00		1.00	6.00	0.60	0.59	0.60	0.05	0.18	
	30.00	45.00		1.00	5.00	0.59	0.50	0.55	0.05	0.14	

Consultant

For M/s. RAM & COMPANY

Partner

Assistant Engineer

Assistant Executive Engineer

Assistant Executive Engineer,
Kodigehalli Sub Division,
Yelahanka Zone, B.B.M.P.,
Bangalore.

(68)

Name Of work : - Improvements to Roads and Drains at Amruthahalli Village, Hoodi Layout, Tala cauvery Layout and Surrounding Areas in Ward No 07 Byatrayanapura, Kodigehalli Sub Division

BOQ Item No	Description Chainage		Side	Nos	L	B1	B2	Avg width	Depth	Quantity	Remarks
	45.00	60.00		1.00	5.00	0.50	0.60	0.55	0.05	0.14	
	60.00	75.00		1.00	7.00	0.60	0.50	0.55	0.05	0.19	
	75.00	90.00		1.00	8.00	0.50	0.49	0.50	0.05	0.20	
	90.00	105.00		1.00	12.00	0.49	0.50	0.50	0.05	0.30	
	105.00	120.00		1.00	13.00	0.50	0.59	0.55	0.05	0.35	
	120.00	135.00		1.00	8.00	0.59	0.60	0.60	0.05	0.24	
	135.00	150.00		1.00	11.00	0.60	0.59	0.60	0.05	0.33	
	150.00	165.00		1.00	5.00	0.59	0.50	0.55	0.05	0.14	
	165.00	180.00		1.00	8.00	0.50	0.50	0.50	0.05	0.20	
	Bad Reaches										
				9.00	2.00			1.30	0.05	1.17	**5th Cross Road-L shape**
				16.00	1.35			1.30	0.05	1.40	
				22.00	0.45			5.00	0.05	2.48	
	Talakaveri Layout- ICICI Bank Road										
	Profile Corection										
	0.00	15.00		1.00	8.00	3.10	3.15	3.13	0.05	1.25	
	15.00	30.00		1.00	7.00	3.15	3.10	3.13	0.05	1.09	
	30.00	45.00		1.00	6.00	3.10	2.95	3.03	0.05	0.91	
	45.00	60.00		1.00	5.00	2.95	2.65	2.80	0.05	0.70	
	60.00	75.00		1.00	4.00	2.65	2.90	2.78	0.05	0.56	
	75.00	90.00		1.00	5.00	2.90	2.70	2.80	0.05	0.70	
	90.00	105.00		1.00	8.00	2.70	2.65	2.68	0.05	1.07	
	105.00	120.00		1.00	7.00	2.65	3.00	2.83	0.05	0.99	
	120.00	135.00		1.00	6.00	3.00	2.95	2.98	0.05	0.89	
	135.00	150.00		1.00	7.00	2.95	3.05	3.00	0.05	1.05	
	150.00	165.00		1.00	5.00	3.05	2.95	3.00	0.05	0.75	
	165.00	180.00		1.00	9.00	2.95	2.65	2.80	0.05	1.26	
	180.00	195.00		1.00	11.00	2.65	2.95	2.80	0.05	1.54	
	195.00	210.00		1.00	5.00	2.95	2.65	2.80	0.05	0.70	
	210.00	225.00		1.00	6.00	2.65	2.85	2.75	0.05	0.83	
	225.00	240.00		1.00	7.00	2.85	2.75	2.80	0.05	0.98	
	240.00	251.00		1.00	8.00	2.75	2.65	2.70	0.05	1.08	
								Total		**75.42**	**Cum**

Consultant

For M/s. RAM & COMPANY

Partner

Assistant Engineer

16/1/18

Assistant Executive Engineer

Assistant Executive Engineer,
Kodigehalli Sub Division,
Yelahanka Zone, B.B.M.P.,
Bangalore.

@ 844.28

(69)

Name Of work : - Improvements to Roads and I ... ahalli Village, Hoodi Layout, Tala cauvery Layout and Surrounding Areas in Ward No 07 Byatrayanap ... Sub Division

BOQ Item No	Description / Chainage		Side	Nos	L	B1	B2	Avg width	Depth	Quantity	Remarks
29	KSRRB M500-19. Providing and laying bituminous concrete 30-40 mm compacted thickness with VG30 Bitumen grade using 40-60 HMP using crushed aggregates of grading II, premixed with bituminous binder at 5.4% of mix and filler, transporting the hot mix to work site, laying with a mechanical paver finisher to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction as per MoRT&H specification clause No. 500.9 complete in all respects as per specifications. MORTH Specification No. 509 (P.No.165 of I.No.21.22.6 in PW,P&IWTD S.R 2016-17)										
	Hoodi Layout 1st Cross Road										
	0.00	15.00		1.00	15.00	4.60	4.90	4.75	0.04	2.85	
	15.00	30.00		1.00	15.00	4.90	4.99	4.95	0.04	2.97	
	30.00	45.00		1.00	15.00	4.99	5.70	5.35	0.04	3.21	
	45.00	60.00		1.00	15.00	5.70	6.39	6.05	0.04	3.63	
	60.00	68.00		1.00	8.00	6.39	6.30	6.35	0.04	2.03	
	Hoodi Layout 2nd Cross Road										
	0.00	15.00		1.00	15.00	6.60	4.79	5.70	0.04	3.42	
	15.00	30.00		1.00	15.00	4.79	5.09	4.94	0.04	2.96	
	30.00	45.00		1.00	15.00	5.09	4.50	4.80	0.04	2.88	
	45.00	60.00		1.00	15.00	4.50	5.20	4.85	0.04	2.91	
	60.00	70.70		1.00	10.70	5.20	2.19	3.70	0.04	3.16	
	Hoodi Layout 3rd Cross Road										
	0.00	15.00		1.00	15.00	4.70	4.59	4.65	0.04	2.79	
	15.00	30.00		1.00	15.00	4.59	4.50	4.55	0.04	2.73	
	30.00	45.00		1.00	15.00	4.50	4.49	4.50	0.04	2.70	
	45.00	70.00		1.00	25.00	4.49	4.10	4.30	0.04	4.30	
	Hoodi Layout 4th Cross Road										
	0.00	15.00		1.00	15.00	5.10	4.50	4.80	0.04	2.88	
	15.00	30.00		1.00	15.00	4.50	5.20	4.85	0.04	2.91	
	30.00	45.00		1.00	15.00	5.20	4.60	4.90	0.04	2.94	
	45.00	60.00		1.00	15.00	4.60	4.29	4.45	0.04	2.67	
	60.00	72.00		1.00	12.00	4.29	4.50	4.40	0.04	2.11	
	Hoodi Layout 5th Cross Road										
	0.00	15.00		1.00	15.00	5.20	4.60	4.90	0.04	2.94	

58.99.

Consultant

For M/s. PAPA & COMPANY

Partner

Assistant Engineer

AE (W4)

28/2

Assistant Executive Engineer

Assistant Executive Engineer,
Kodigehalli Sub Division,
Yelahanka Zone, B.B.M.P.,
Bangalore.

(76)

Name Of work : - Improvements to Roads and Drains at Amruthahalli Village, Hoodi Layout, Tala cauvery Layout and Surrounding Areas in Ward No 07 Byatrayanapura, Kodigehalli Sub Division

BOQ Item No	Description Chainage		Side	Nos	L	B1	B2	Avg width	Depth	58.99 Quantity	Remarks
	15.00	30.00		1.00	15.00	4.60	5.10	4.85	0.04	2.91	
	30.00	45.00		1.00	15.00	5.10	4.29	4.70	0.04	2.82	
	45.00	60.00		1.00	15.00	4.29	4.40	4.35	0.04	2.61	
	60.00	71.00		1.00	11.00	4.40	4.50	4.45	0.04	1.96	
	Hoodi Layout 5th Cross Road-L shape										
	0.00	15.00		1.00	15.00	4.90	4.99	4.95	0.04	2.97	
	15.00	30.00		1.00	15.00	4.99	5.50	5.25	0.04	3.15	
	30.00	45.00		1.00	15.00	5.50	5.50	5.50	0.04	3.30	
	45.00	60.00		1.00	15.00	5.50	4.70	5.10	0.04	3.06	
	60.00	75.00		1.00	15.00	4.70	4.90	4.80	0.04	2.88	
	75.00	90.00		1.00	15.00	4.90	5.40	5.15	0.04	3.09	
	90.00	105.00		1.00	15.00	5.40	4.50	4.95	0.04	2.97	
	105.00	120.00		1.00	15.00	4.50	4.30	4.40	0.04	2.64	
	120.00	135.00		1.00	15.00	4.30	4.50	4.40	0.04	2.64	
	135.00	150.00		1.00	15.00	4.50	4.90	4.70	0.04	2.82	
	150.00	165.00		1.00	15.00	4.90	4.90	4.90	0.04	2.94	
	165.00	180.00		1.00	15.00	4.90	5.49	5.20	0.04	3.12	
	180.00	195.00		1.00	15.00	5.49	5.30	5.40	0.04	3.24	
	195.00	209.00		1.00	14.00	5.30	5.50	5.40	0.04	3.02	
	Hoodi Layout Main Road										
	0.00	15.00		1.00	15.00	6.70	6.60	6.65	0.04	3.99	
	15.00	30.00		1.00	15.00	6.60	6.10	6.35	0.04	3.81	
	30.00	45.00		1.00	15.00	6.10	6.10	6.10	0.04	3.66	
	45.00	60.00		1.00	15.00	6.10	6.40	6.25	0.04	3.75	
	60.00	75.00		1.00	15.00	6.40	6.19	6.30	0.04	3.78	
	75.00	90.00		1.00	15.00	6.19	5.60	5.90	0.04	3.54	
	90.00	105.00		1.00	15.00	5.60	5.20	5.40	0.04	3.24	
	105.00	120.00		1.00	15.00	5.20	4.80	5.00	0.04	3.00	
	120.00	141.00		1.00	21.00	4.80	5.20	5.00	0.04	4.20	
	141.00	156.00		1.00	15.00	5.20	6.30	5.75	0.04	3.45	
	156.00	171.00		1.00	15.00	6.30	6.40	6.35	0.04	3.81	
	171.00	185.00		1.00	14.00	6.40	6.40	6.40	0.04	3.58	
	185.00	200.00		1.00	15.00	6.40	6.50	6.45	0.04	3.87	
	200.00	215.00		1.00	15.00	6.50	6.90	6.70	0.04	4.02	
	215.00	230.00		1.00	15.00	6.90	6.90	6.90	0.04	4.14	
	230.00	245.00		1.00	15.00	6.90	5.20	6.05	0.04	3.63	

Consultant

For M/s. RAM & COMPANY

Partner

Assistant Engineer

A.E(W)
28/2

Assistant Executive Engineer

Assistant Executive Engineer.
Kodigehalli Sub Division,
Yelahanka Zone, B.B.M.P.,
Bangalore.

(71)

Name Of work : - Improvements to Roads and Drains at Amruthahalli Village, Hoodi Layout, Tala cauvery Layout and Surrounding Areas in Ward No 07 Byatrayanapura, Kodigehalli Sub Division

BOQ Item No	Description Chainage		Side	Nos	L	B1	B2	Avg width	Depth	Quantity	Remarks
	245.00	260.00		1.00	15.00	5.20	5.60	5.40	0.04	3.24	
	260.00	275.00		1.00	15.00	5.60	4.70	5.15	0.04	3.09	
	275.00	290.00		1.00	15.00	4.70	5.30	5.00	0.04	3.00	
	290.00	305.00		1.00	15.00	5.30	5.50	5.40	0.04	3.24	
	305.00	320.00		1.00	15.00	5.50	5.00	5.25	0.04	3.15	
	320.00	334.00		1.00	14.00	5.00	4.90	4.95	0.04	2.77	
	Talakaveri Layout- SBI Bank Road										
	0.00	15.00		1.00	15.00	7.50	7.20	7.35	0.04	4.41	
	15.00	30.00		1.00	15.00	7.20	8.30	7.75	0.04	4.65	
	30.00	45.00		1.00	15.00	8.30	8.50	8.40	0.04	5.04	
	45.00	60.00		1.00	15.00	8.50	7.80	8.15	0.04	4.89	
	60.00	75.00		1.00	15.00	7.80	5.90	6.85	0.04	4.11	
	75.00	90.00		1.00	15.00	5.90	6.49	6.20	0.04	3.72	
	90.00	105.00		1.00	15.00	6.49	6.50	6.50	0.04	3.90	
	105.00	120.00		1.00	15.00	6.50	7.90	7.20	0.04	4.32	
	120.00	135.00		1.00	15.00	7.90	6.50	7.20	0.04	4.32	
	135.00	150.00		1.00	15.00	6.50	6.80	6.65	0.04	3.99	
	150.00	165.00		1.00	15.00	6.80	7.60	7.20	0.04	4.32	
	165.00	180.00		1.00	15.00	7.60	7.40	7.50	0.04	4.50	
	180.00	195.00		1.00	15.00	7.40	7.19	7.30	0.04	4.38	
	195.00	222.00		1.00	27.00	7.19	8.00	7.60	0.04	8.20	
	222.00	264.00		1.00	42.00	8.00	7.50	7.75	0.04	13.02	
	Talakaveri Layout- ICICI Bank Road										
	0.00	15.00		1.00	15.00	4.90	7.10	6.00	0.04	3.60	
	15.00	30.00		1.00	15.00	7.10	7.49	7.30	0.04	4.38	
	30.00	45.00		1.00	15.00	7.49	8.50	8.00	0.04	4.80	
	45.00	60.00		1.00	15.00	8.50	7.90	8.20	0.04	4.92	
	60.00	75.00		1.00	15.00	7.90	8.19	8.05	0.04	4.83	
	75.00	90.00		1.00	15.00	8.19	7.70	7.95	0.04	4.77	
	90.00	105.00		1.00	15.00	7.70	7.90	7.80	0.04	4.68	
	105.00	120.00		1.00	15.00	7.90	7.99	7.95	0.04	4.77	
	120.00	135.00		1.00	15.00	7.99	7.60	7.80	0.04	4.68	
	135.00	150.00		1.00	15.00	7.60	6.50	7.05	0.04	4.23	
	150.00	165.00		1.00	15.00	6.50	5.40	5.95	0.04	3.57	
	165.00	180.00		1.00	15.00	5.40	5.50	5.45	0.04	3.27	
	180.00	195.00		1.00	15.00	5.50	5.40	5.45	0.04	3.27	

Consultant

For M/s. R A M & COMPANY

Partner

Assistant Engineer

AE(Civil)

28/2

Assistant Executive Engineer

Assistant Executive Engineer
Kodigehalli Sub Division,
Yelahanka Zone, B.B.M.P.,
Bangalore.

(72)

Name Of work : - Improvements to Roads and Drains at Amruthahalli Village, Hoodi Layout, Tala cauvery Layout and Surrounding Areas in Ward No 07 Byatrayanapura, Kodigehalli Sub Division

BOQ Item No	Description Chainage		Side	Nos	L	B1	B2	Avg width	Depth	Quantity	Remarks
	195.00	210.00		1.00	15.00	5.40	5.80	5.60	0.04	3.36	
	210.00	225.00		1.00	15.00	5.80	5.70	5.75	0.04	3.45	
	225.00	240.00		1.00	15.00	5.70	6.09	5.90	0.04	3.54	
	240.00	251.00		1.00	11.00	6.09	6.60	6.35	0.04	2.79	
	Talcauvery Main Road 4th Cross Road										
	0.00	15.00		1.00	15.00	8.75	7.75	8.25	0.04	4.95	
	15.00	30.00		1.00	15.00	7.75	7.85	7.80	0.04	4.68	
	30.00	45.00		1.00	15.00	7.85	7.55	7.70	0.04	4.62	
	45.00	60.00		1.00	15.00	7.55	6.94	7.25	0.04	4.35	
	60.00	75.00		1.00	15.00	6.94	8.75	7.85	0.04	4.71	
	75.00	90.00		1.00	15.00	8.75	7.14	7.95	0.04	4.77	
	90.00	105.00		1.00	15.00	7.14	7.55	7.35	0.04	4.41	
	105.00	120.00		1.00	15.00	7.55	7.44	7.50	0.04	4.50	
	120.00	135.00		1.00	15.00	7.44	7.55	7.50	0.04	4.50	
	135.00	150.00		1.00	15.00	7.55	9.65	8.60	0.04	5.16	
	150.00	165.00		1.00	15.00	9.65	7.54	8.60	0.04	5.16	
	165.00	180.00		1.00	15.00	7.54	7.75	7.65	0.04	4.59	
	180.00	195.00		1.00	15.00	7.75	8.54	8.15	0.04	4.89	
	195.00	210.00		1.00	15.00	8.54	7.85	8.20	0.04	4.92	
	210.00	230.00		1.00	20.00	7.85	8.84	8.35	0.04	6.68	
	Chitrakut Apt Road										
	0.00	15.00		1.00	15.00	5.70	5.29	5.50	0.04	3.30	
	15.00	30.00		1.00	15.00	5.29	6.20	5.75	0.04	3.45	
	30.00	45.00		1.00	15.00	6.20	4.50	5.35	0.04	3.21	
	45.00	47.00		1.00	2.00	4.50	6.00	5.25	0.04	0.42	
	Govindappa badavane 1st Cross Road										
	0.00	15.00		1.00	15.00	6.50	5.10	5.80	0.04	3.48	
	15.00	30.00		1.00	15.00	5.10	6.20	5.65	0.04	3.39	
	30.00	45.00		1.00	15.00	6.20	6.30	6.25	0.04	3.75	
	45.00	57.00		1.00	12.00	6.30	6.30	6.30	0.04	3.02	
	Hoodi badavane 2nd main Road										
	0.00	15.00		1.00	15.00	4.10	4.10	4.10	0.04	2.46	

Consultant

For M/s RAM & COMPANY

Partner

Assistant Engineer

AE(WZ)
28/2

Assistant Executive Engineer

Assistant Executive Engineer
Kodigehalli Sub Division
Yelahanka Zone, B.B.M.P.,
Bangalore.

(73)

Name Of work : - Improvements to Roads and Drains at Amruthahalli Village, Hoodi Layout, Tala cauvery Layout and Surrounding Areas in Ward No 07 Byatrayanapura, Kodigehalli Sub Division

BOQ Item No	Description Chainage		Side	Nos	L	B1	B2	Avg width	Depth	Quantity	Remarks
	15.00	30.00		1.00	15.00	4.10	3.70	3.90	0.04	2.34	
	30.00	45.00		1.00	15.00	3.70	3.50	3.60	0.04	2.16	
	45.00	60.00		1.00	15.00	3.50	3.70	3.60	0.04	2.16	
	60.00	75.00		1.00	15.00	3.70	4.40	4.05	0.04	2.43	
	75.00	90.00		1.00	15.00	4.40	4.30	4.35	0.04	2.61	
	90.00	99.00		1.00	9.00	4.30	4.50	4.40	0.04	1.58	
							Total Quantity			**448.32**	**Cum**
	Add cost of Waste Plastic @ 8% of Bitumen Weight										
	Bitumen = 141 kg/cum						**Total Qty**			**5057.05**	**Kgs**
37	KSRRB M800-13. Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads at 250 gms per sqm area, thickness of 2.5mm is exclusive of surface applied glass beads as per IRC:35. The finished surface to be level, uniform and free from streaks and holes complete as per specifications. MORTH Specification No. 803. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work										
	Hoodi layout 1st Cross Road - CENTER LINE			11	3	0.1				3.3	
	Hoodi layout 2nd Cross Road - CENTER LINE			12	3	0.1				3.6	
	Hoodi layout 3rd Cross Road - CENTER LINE			12	3	0.1				3.6	
	Hoodi layout 4th Cross Road - CENTER LINE			12	3	0.1				3.6	
	Hoodi layout 5th Cross Road - CENTER LINE			12	3	0.1				3.6	
	Hoodi layout 5th Cross Road-L shape-CENTRE LINE			35	3	0.1				10.5	
	Govindappa badavane 1st Cross Road-CENTRE LINE			10	3	0.1				3	
	Hoodi badavane 2nd main Road -CENTRE LINE			16	3	0.1				4.8	
	Chitrakut Apt Road-CENTER LINE			8	3	0.1				2.4	
	Talcauvery Main Road 4th Cross Road - EDGE LINE			2	230	0.1				46	

Consultant

For M/s. RAM & COMPANY

Partner

Assistant Engineer

AE(W7) 28/2

Assistant Executive Engineer

Kodigehalli Sub Division,
Yelahanka Zone, B.B.M.P.,
Bangalore.

(14)

Name Of work : - Improvements to Roads and Drains at Amruthahalli Village, Hoodi Layout, Tala cauvery Layout and Surrounding Areas in Ward No 07 Byatrayanapura, Kodigehalli Sub Division

BOQ Item No	Description / Chainage	Side	Nos	L	B1	B2	Avg width	Depth	Quantity	Remarks
	Talcauvery Main Road 4th Cross Road-CENTER LINE				38	3	0.1		11.4	
	Hoodi Layout Main Road-EDGE LINE				2	334	0.1		66.8	
	Hoodi Layout Main Road-CENTER LINE				57	3	0.1		17.1	
	Talacuavery Layout Main Road Beside SBI Bank-EDGE LINE				2	264	0.1		52.8	
	Talacuavery Layout Main Road Beside SBI Bank-CENTER LINE				44	3	0.1		13.2	
	Talacuavery Layout Main Road Beside ICICI Bank-EDGE LINE				2	251	0.1		50.2	
	Talacuavery Layout Main Road Beside ICICI Bank-CENTER LINE				42	3	0.1		12.6	
						Total Qty in Sqm			**308.5**	

Consultant

For M/s RAM & COMPANY

Partner

Assistant Engineer

AE(NZ)

20/2/18

Assistant Executive Engineer

Assistant Executive Engine
Kodigehalli Sub Divisio
Yelahanka Zone, B.B.M.P.
Bangalore.

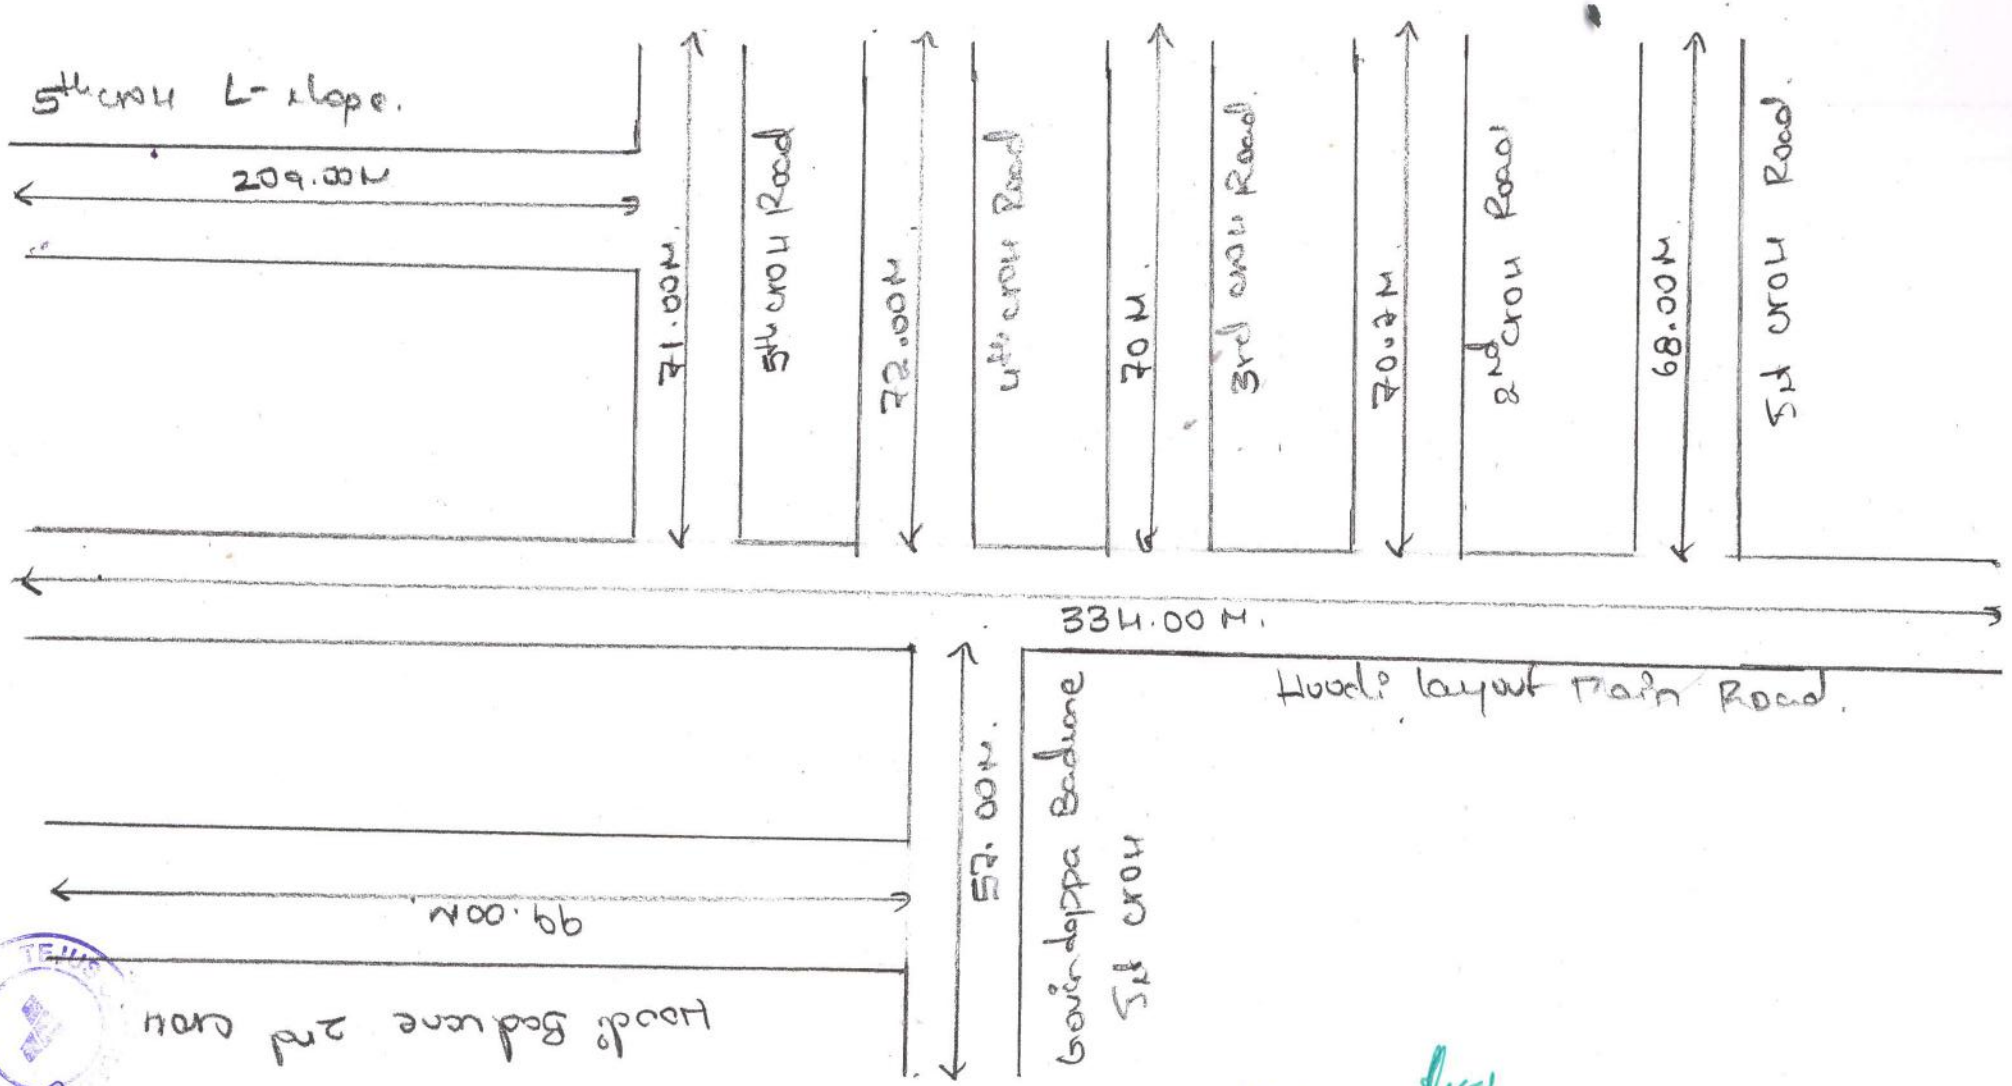

Assistant Executive Engineer.
Kodigehalli Sub Division
Yelahanka

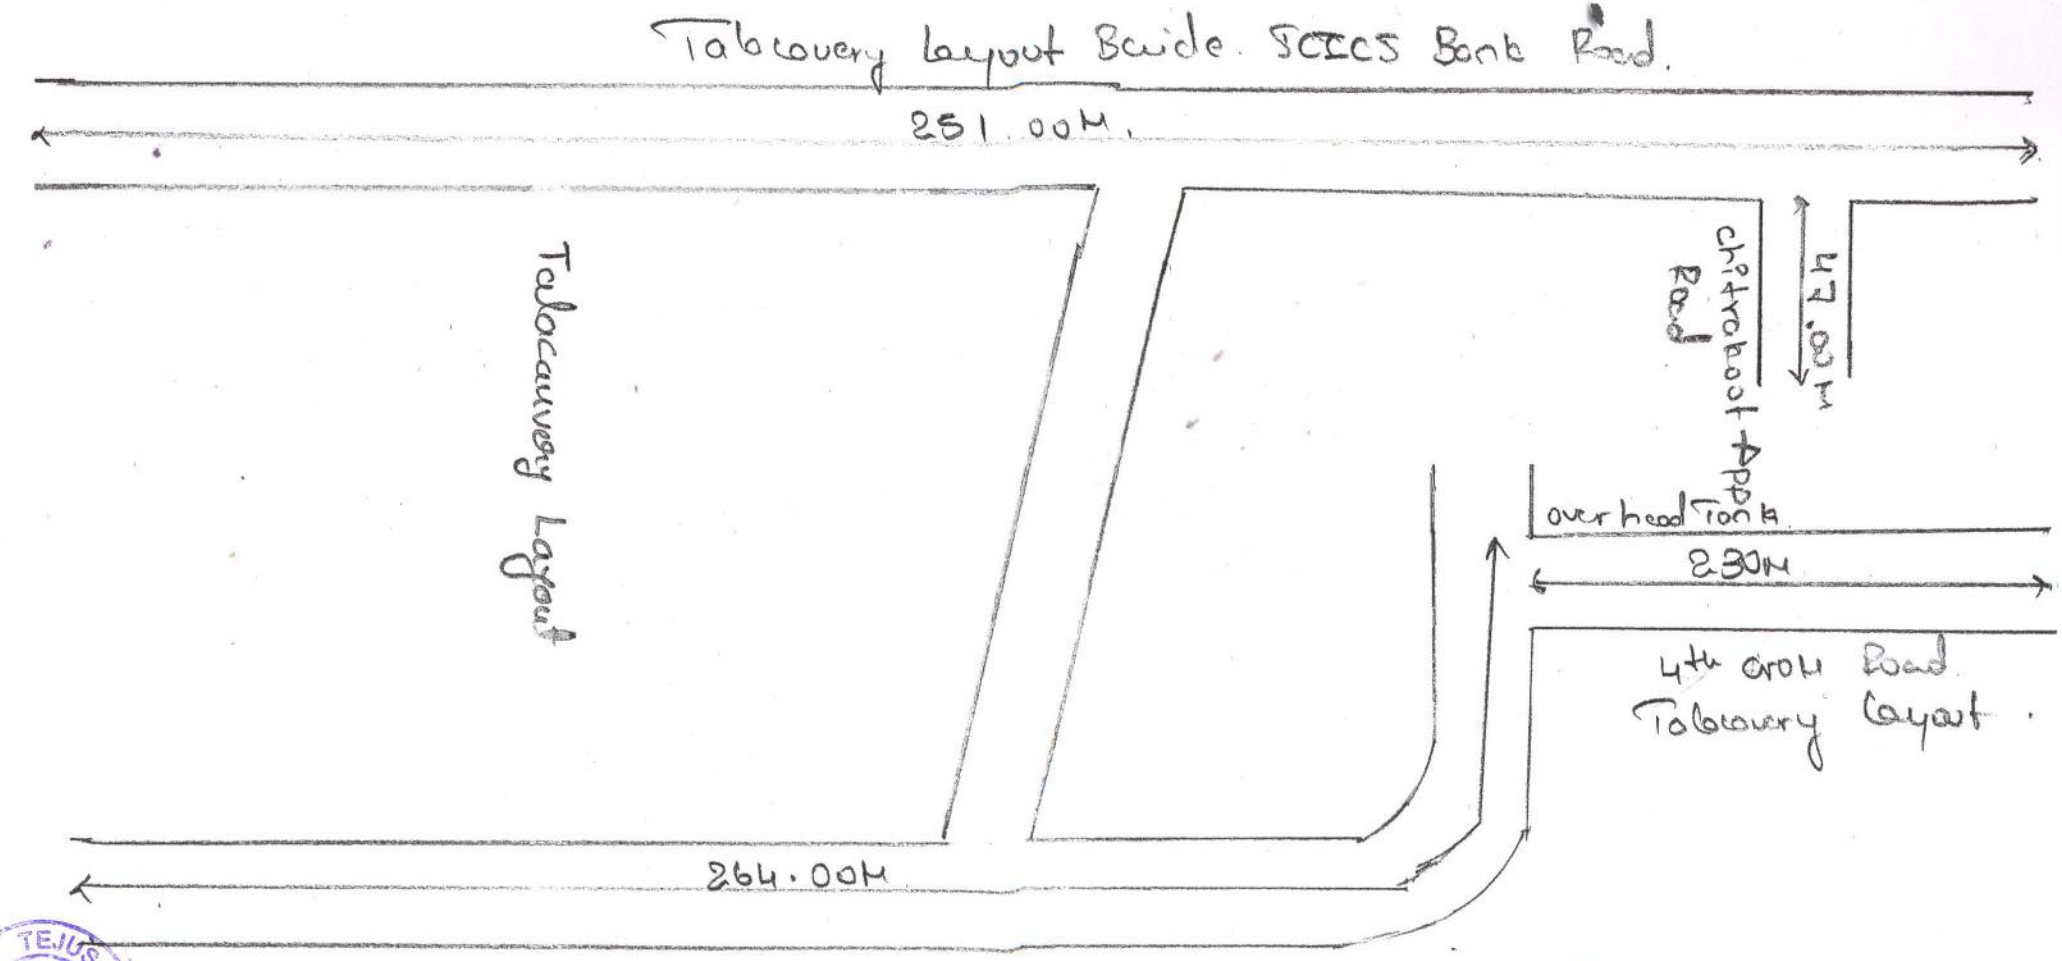

TEJUS CONSULTANTS

Assistant Executive Engineer,
Kodigehalli Sub Division,
Yelahanka Zone, B.B.M.P.,
Bangalore.
